



Erosion Contract 2 Before Construction



American River Common Features 2016 Sacramento River Levees Monthly Update

July 2023

Highlights (last 30 days)

2023 construction is underway and SREL Contracts 3 and 4 are in progress. We'll begin Erosion Contract 2 - Season 1 early this month. We completed the majority of the tree clearing in preparation for Erosion Contract 2 - Season 1 on June 29. Eight remaining trees will be removed around August 15 when we expect an active nest of Osprey juveniles to have developed enough to leave the area. Design efforts are on track for construction in 2024 (Erosion C4) and, 2025/2026 (Erosion C3).

Looking Ahead (next 30+ days)

What can I expect?

Cutoff wall test section construction, evaluation of post-storm related damage, batch plant mobilization, material deliveries, and tree removal/site preparation for 2023 erosion with appropriate environmental monitoring.

Hours of Operation: Mon – Sat from 7am-7pm.

Garcia Bend Park Staging

- ◆ Boat ramp closed during construction at the request of the City with intermittent vehicle traffic during construction.
- ◆ 10-20 truck loads of material for approximately 10 consecutive days
- ◆ Following the construction of a test section, Garcia Park will have light traffic in and out until mid to late July.

Sump 132

- ◆ Work anticipated to continue through December
- ◆ Batch plant operations
- ◆ 2-3 cement deliveries daily

Benham Way Staging Area/North Point Way Access Point

- ◆ Completed and reopened

Zacharias Park

- ◆ Completed and reopened

Cliff's Marina

- ◆ Temporary fencing installation. Construction activity beginning mid-May and continuing until December. The levee is closed from the Freeport Water Tower to Cliff's Marina.
- ◆ Haul trucks entering/existing

Westin

- ◆ Levee work continues through December
- ◆ Batch plant mobilization and the begin of test wall construction
- ◆ Deep Mixed Method drilling moving south from Sump 132

Broadway

- ◆ We don't anticipate work starting until late summer/early fall

Question of the Month

Where and when will Erosion Contract 2 occur and what construction method will be used?

Contract 2 consists of erosion control and bank stabilization improvements at six sites along a 3-mile stretch of the Sacramento River's East Levee from the Pioneer Bridge to the Pocket. We'll construct sites 2, 3 and 6 this year and sites 1, 4 and 5 in 2024 (see construction map on page 3). In-water construction will begin this month and our crew will work from tug and barge on the waterside of levee, which may affect boating traffic.

Information Resources:

Project Webpage:

www.sacleveeupgrades.com



Sacramento District Homepage:

www.spk.usace.army.mil

Contact Information:

For questions or concerns, please contact our Public Affairs Office at
916-557-5100
spk-pao@usace.army.mil

Upcoming Milestones

Seepage/Stability/ Overtopping

SREL Contract 3

Construction

March 2022 - September 2023

SREL Contract 4

Construction

April 2023 - December 2023

Erosion

Contract 2

Construction

July 2023 - October 2024

Contract 3

Construction award

anticipated January/February
2025

Contract 4


Construction award

anticipated January/February
2024

Additional information can be found on
our project web page at
www.sacleveeupgrades.com

*All Dates Subject to Change

SREL Contract 4 Construction Map

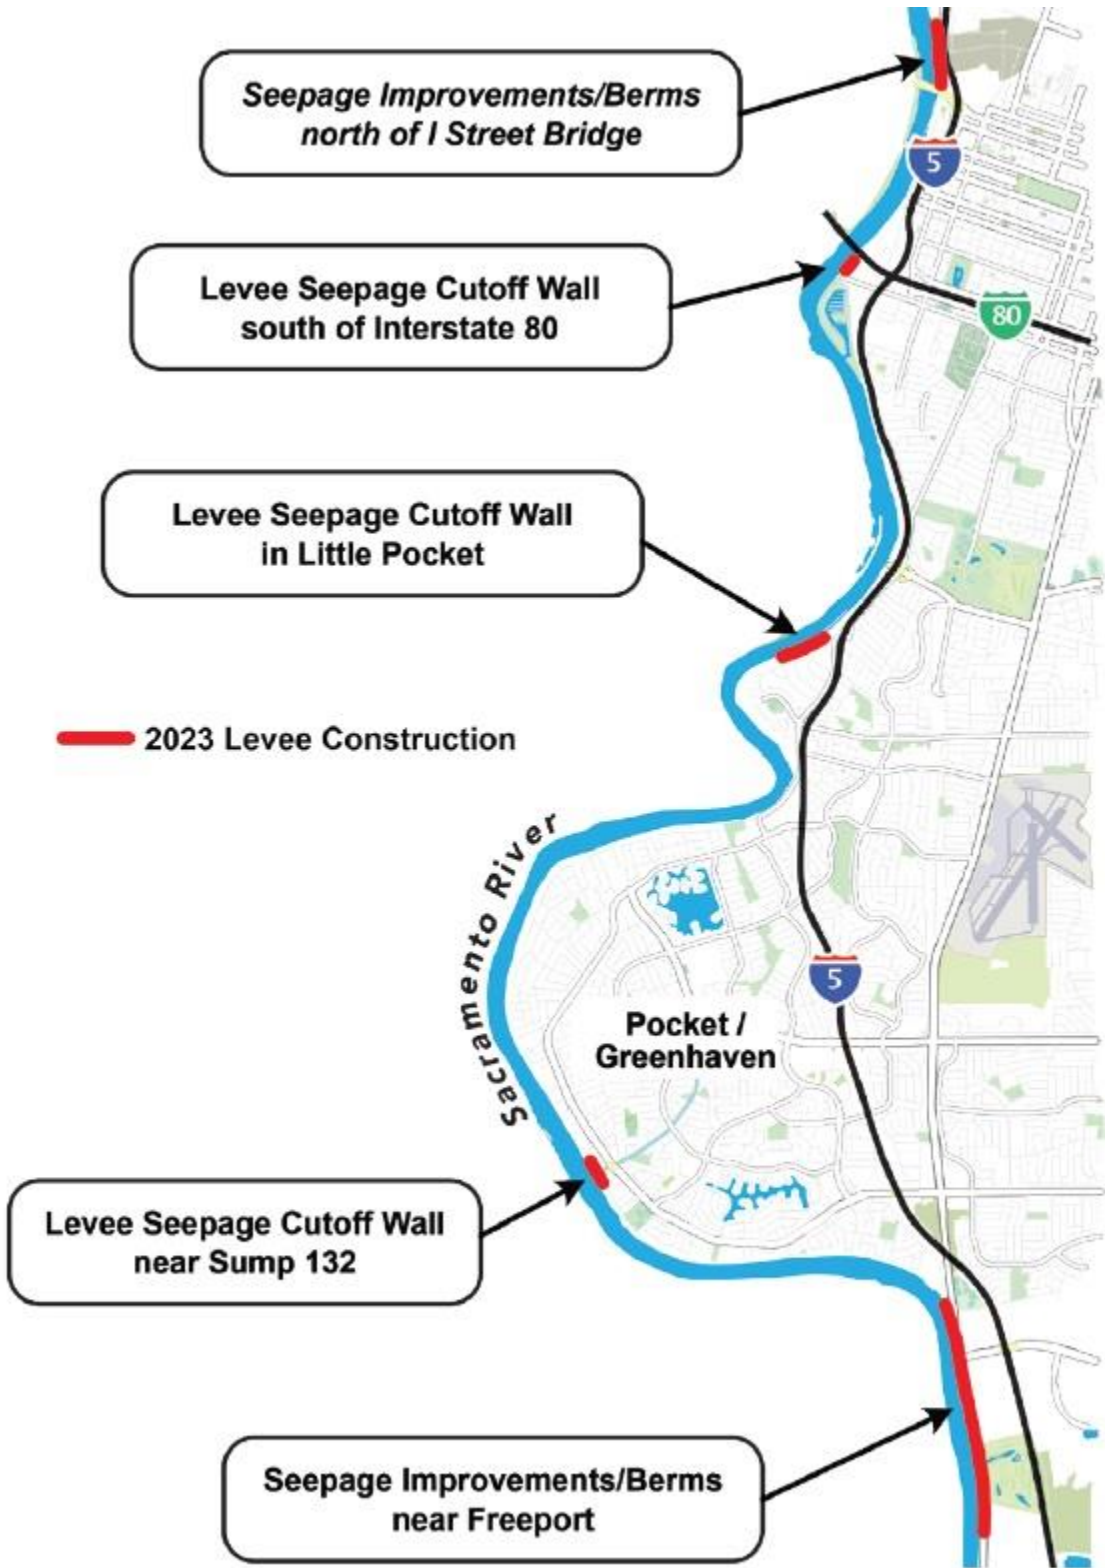

Erosion C2 Construction Map

